


PLAINVILLE SQUARE - BEER GARDEN

111 SOUTH STREET PLAINVILLE, MA


EXHIBIT NUMBER

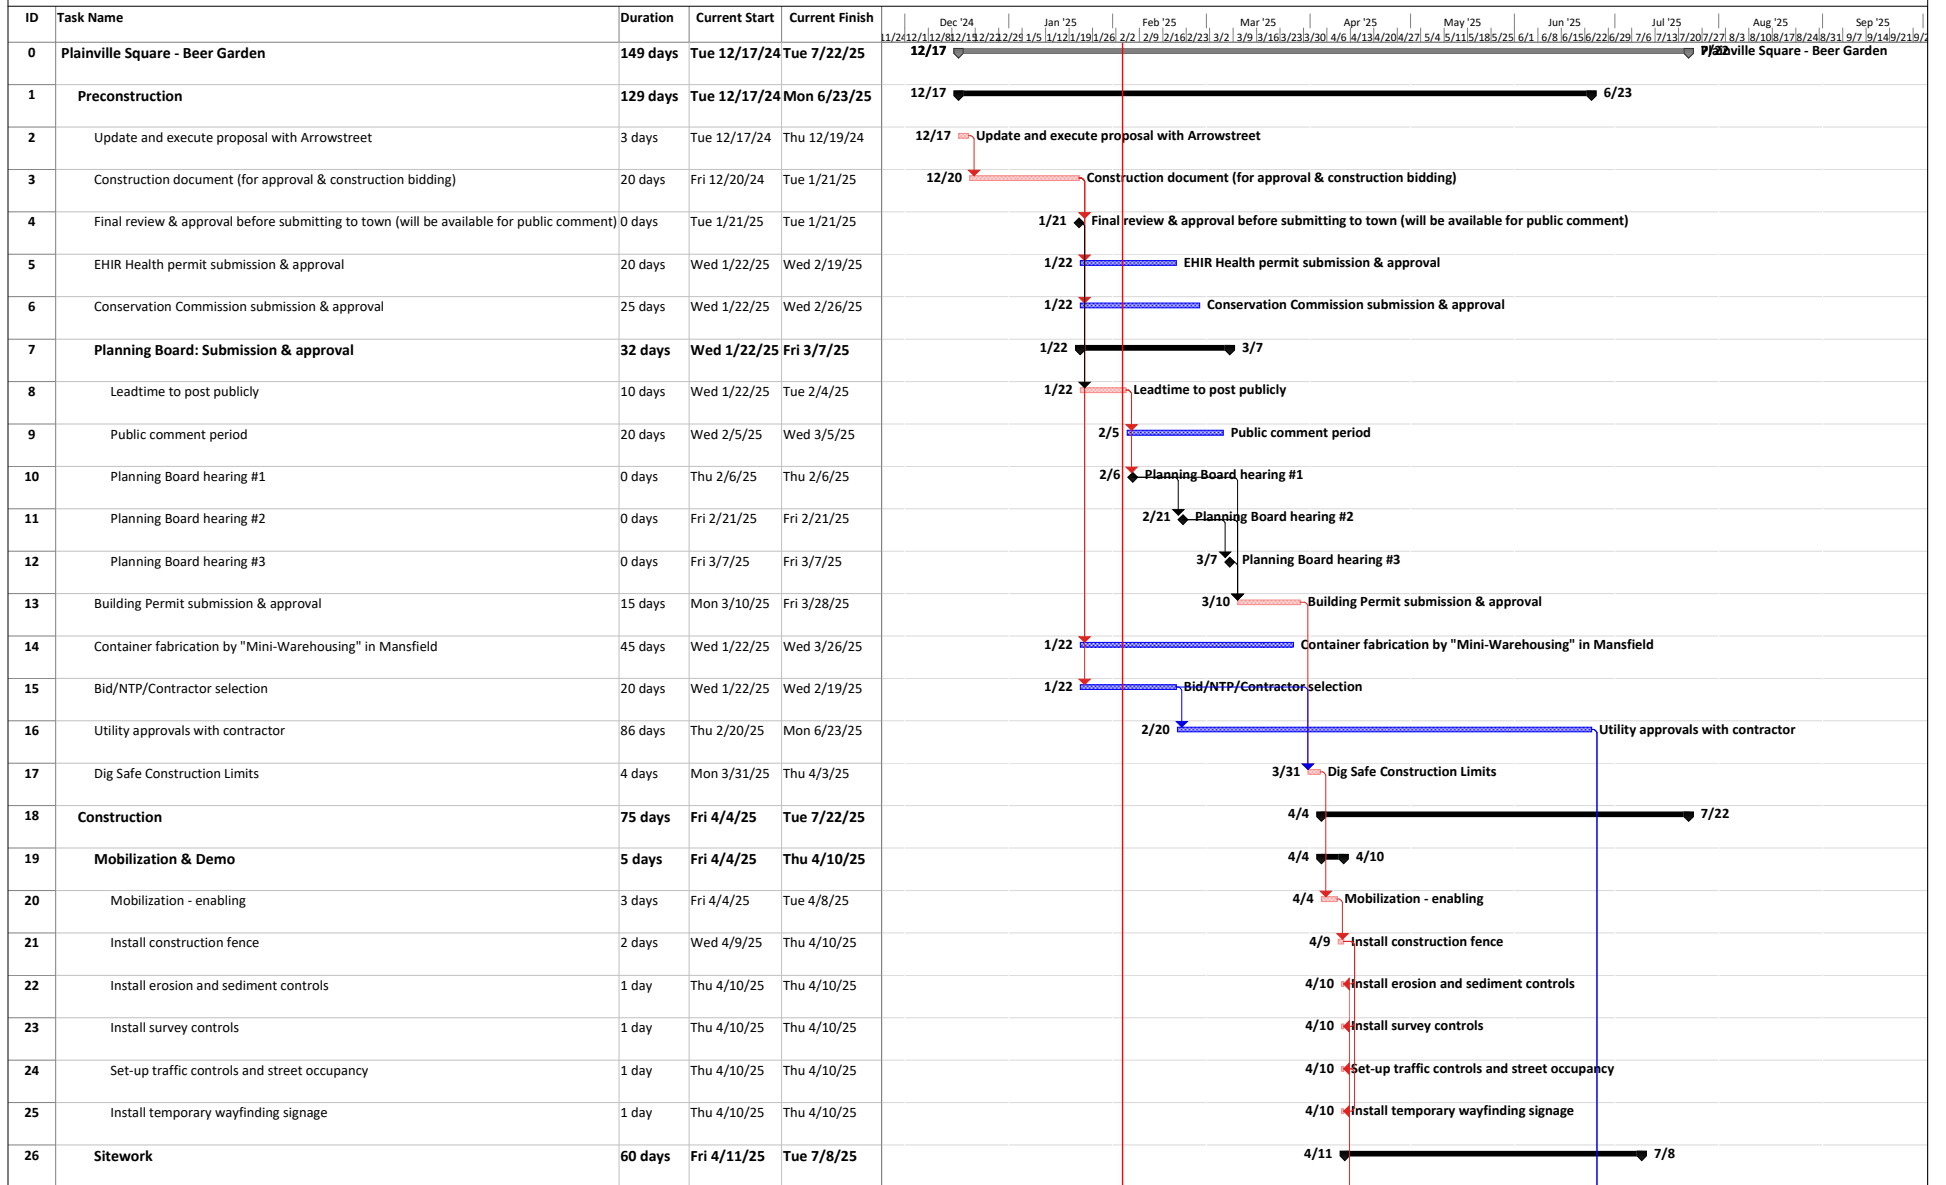

PLAINVILLE SQUARE - BEER GARDEN

111 SOUTH STREET PLAINVILLE, MA

EXHIBIT NUMBER

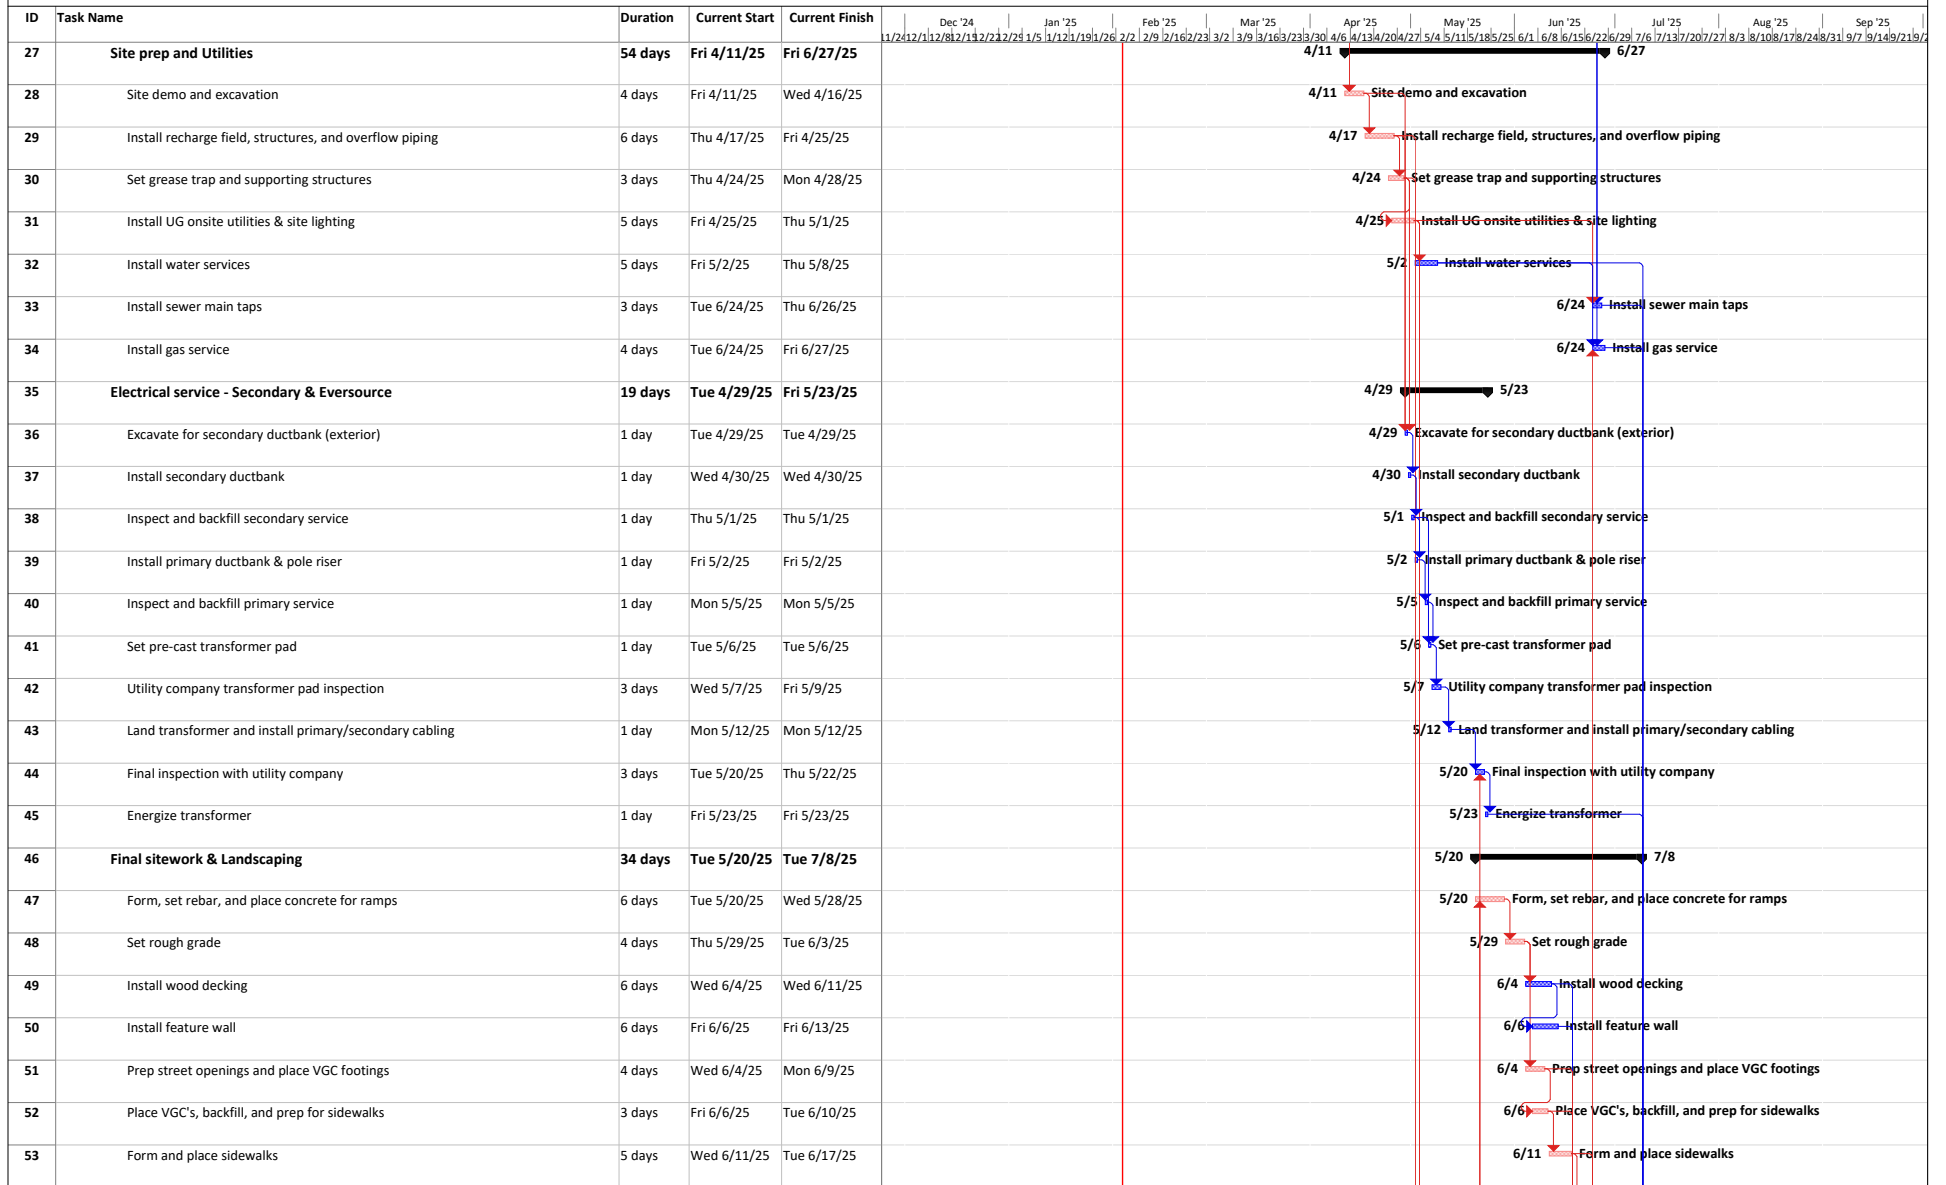

PLAINVILLE SQUARE - BEER GARDEN

111 SOUTH STREET PLAINVILLE, MA

EXHIBIT NUMBER

ID	Task Name	Duration	Current Start	Current Finish	Dec '24	Jan '25	Feb '25	Mar '25	Apr '25	May '25	Jun '25	Jul '25	Aug '25	Sep '25
54	Final grading	4 days	Wed 6/18/25	Mon 6/23/25							6/18	Final grading		
55	Spread loam	1 day	Tue 6/24/25	Tue 6/24/25							6/24	Spread loam		
56	Install irrigation	1 day	Wed 6/25/25	Wed 6/25/25							6/25	Install irrigation		
57	Install raised plantings and hardscapes	1 day	Tue 6/24/25	Tue 6/24/25							6/24	Install raised plantings and hardscapes		
58	Install landscaping and complete irrigation	1 day	Thu 6/26/25	Thu 6/26/25							6/26	Install landscaping and complete irrigation		
59	Install finish ground materials	4 days	Fri 6/27/25	Wed 7/2/25							6/27	Install finish ground materials		
60	Fine grade for paving	2 days	Tue 7/1/25	Wed 7/2/25							7/1	Fine grade for paving		
61	Install binder	1 day	Thu 7/3/25	Thu 7/3/25							7/3	Install binder		
62	Install final paving	1 day	Mon 7/7/25	Mon 7/7/25							7/7	Install final paving		
63	Line stripping and signage	1 day	Tue 7/8/25	Tue 7/8/25							7/8	Line stripping and signage		
64	Prefab Building - Foundations, Utility prep, & Building Placement	12 days	Fri 5/2/25	Mon 5/19/25						5/2	5/19			
65	Excavate for prefab building SOG's	2 days	Fri 5/2/25	Mon 5/5/25						5/2	Excavate for prefab building SOG's			
66	Install UG utilities and stub-ups	3 days	Tue 5/6/25	Thu 5/8/25						5/6	Install UG utilities and stub-ups			
67	Form, set rebar, and place concrete for SOG's	3 days	Fri 5/9/25	Tue 5/13/25						5/9	Form, set rebar, and place concrete for SOG's			
68	Strip forms and backfill to rough grade	2 days	Wed 5/14/25	Thu 5/15/25						5/14	Strip forms and backfill to rough grade			
69	Set pre-fab units and tie-in utilities	2 days	Fri 5/16/25	Mon 5/19/25						5/16	Set pre-fab units and tie-in utilities			
70	Final Inspections, Close-out, Commissioning	10 days	Wed 7/9/25	Tue 7/22/25							7/9	7/22		
71	Final Inspections	9 days	Wed 7/9/25	Mon 7/21/25							7/9	7/21		
72	GSA/DPW final sign-off	1 day	Wed 7/9/25	Wed 7/9/25							7/9	GSA/DPW final sign-off		
73	Plumbing Final	1 day	Thu 7/10/25	Thu 7/10/25							7/10	Plumbing Final		
74	Electrical Final	1 day	Thu 7/10/25	Thu 7/10/25							7/10	Electrical Final		
75	HVAC Final	1 day	Thu 7/10/25	Thu 7/10/25							7/10	HVAC Final		
76	Fire Dept. Final	2 days	Fri 7/11/25	Mon 7/14/25							7/11	Fire Dept. Final		
77	Building Dept. Final	1 day	Tue 7/15/25	Tue 7/15/25							7/15	Building Dept. Final		
78	Apply for certificate of occupancy	3 days	Wed 7/16/25	Fri 7/18/25							7/16	Apply for certificate of occupancy		
79	Receive Certificate of Occupancy	1 day	Mon 7/21/25	Mon 7/21/25							7/21	Receive Certificate of Occupancy		
80														

PLAINVILLE SQUARE - BEER GARDEN
111 SOUTH STREET PLAINVILLE, MA

EXHIBIT NUMBER

ID	Task Name	Duration	Current Start	Current Finish	1/2412/11/2/812/13/2/23/2/23/1/5/1/12/1/19/1/26/2/2/2/9/2/16/2/23/3/2/3/9/3/16/3/23/3/30/4/6/4/13/4/20/4/27/5/4/5/11/5/18/5/25/6/1/6/8/6/15/6/22/6/29/7/6/7/13/7/20/7/27/8/3/8/10/8/17/8/24/8/31/9/7/9/14/9/21/9/28/
81	Turnover	1 day	Tue 7/22/25	Tue 7/22/25	7/22 ▼ Turnover
