





BU 113 BAY STATE ROAD



BU 113 BAY STATE ROAD

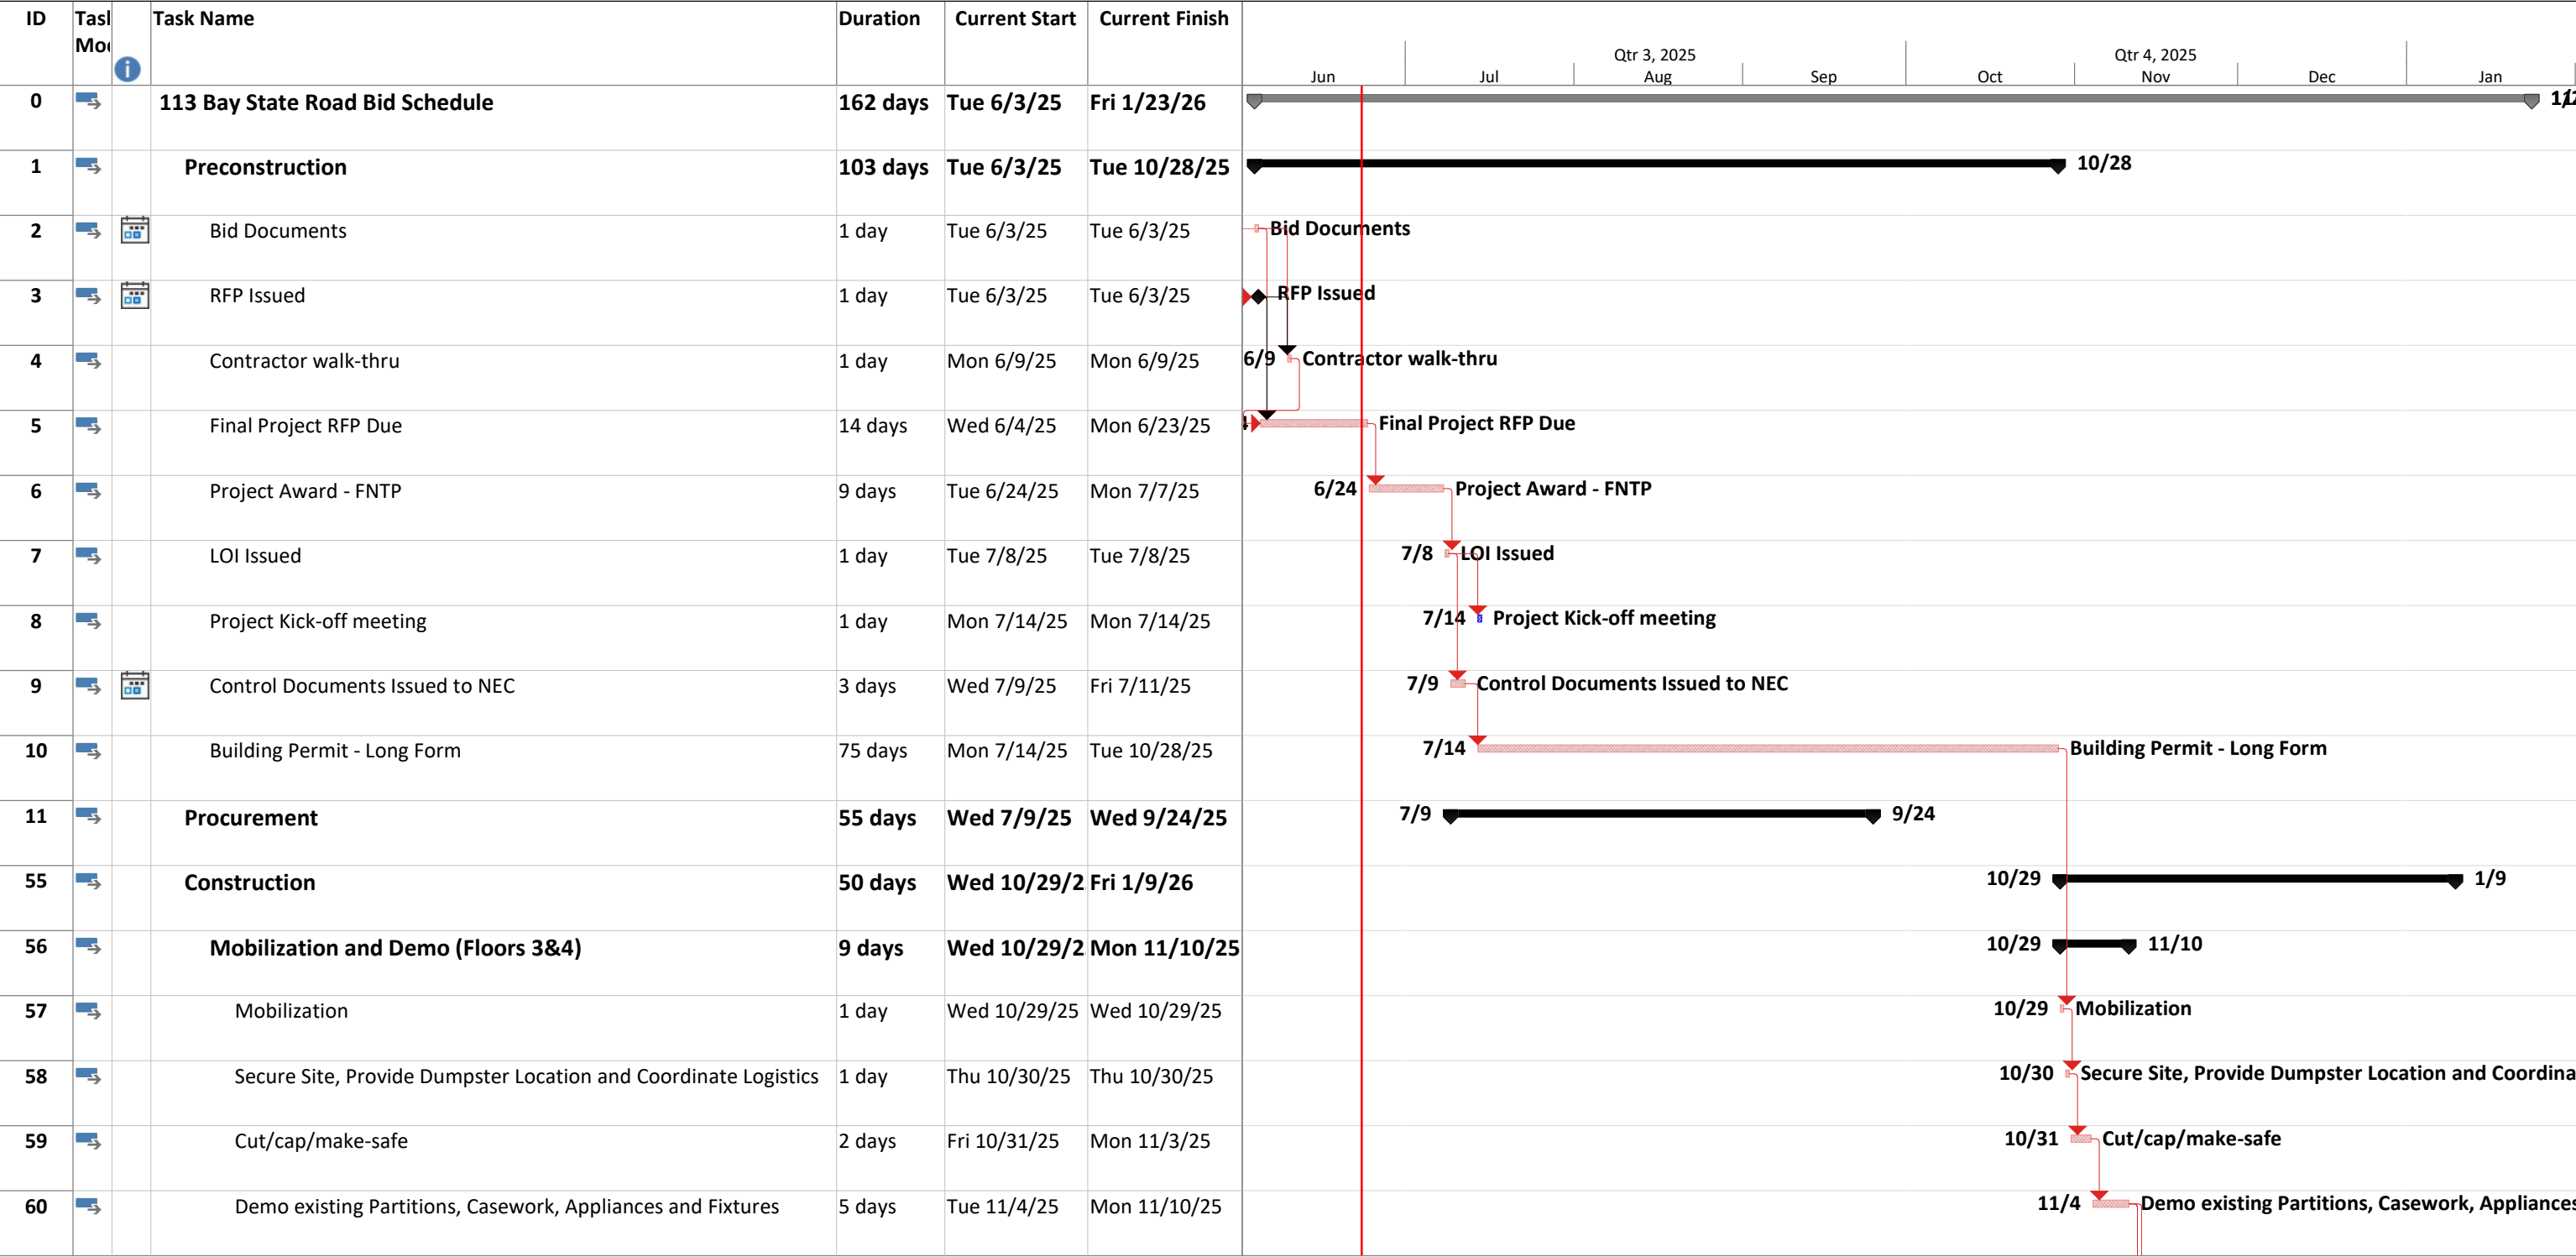

ID	Task Name	Duration	Current Start	Current Finish	<div><div>Jun</div><div>Jul</div><div>Qtr 3, 2025 Aug</div><div>Sep</div><div>Oct</div><div>Qtr 4, 2025 Nov</div><div>Dec</div><div>Jan</div></div>											
79	Final clean	1 day	Wed 1/7/26	Wed 1/7/26											1/7	Final clean
80	Punchlist	2 days	Thu 1/8/26	Fri 1/9/26											1/8	Punchlist
81	Final Inspections, Close-out, Commissioning	14 days	Mon 1/5/26	Fri 1/23/26											1/5	1/23
82	Commissioning	4 days	Tue 1/6/26	Fri 1/9/26											1/6	1/9
83	Factory Startup Equipment	1 day	Tue 1/6/26	Tue 1/6/26											1/6	Factory Startu
84	Programming and Controls	1 day	Wed 1/7/26	Wed 1/7/26											1/7	Programming
85	Balancing Systems	1 day	Thu 1/8/26	Thu 1/8/26											1/8	Balancing Sy
86	Balancing reports	1 day	Fri 1/9/26	Fri 1/9/26											1/9	Balancing re
87	Final Inspections	14 days	Mon 1/5/26	Fri 1/23/26											1/5	1/23
88	Plumbing Affidavit from design team	1 day	Tue 1/6/26	Tue 1/6/26											1/6	Plumbing Affi
89	Electrical/FA Affidavit from design team	1 day	Mon 1/5/26	Mon 1/5/26											1/5	Electrical/FA A
90	Mechanical Affidavit from design team	1 day	Mon 1/12/26	Mon 1/12/26											1/12	Mechanica
91	Architectural Affidavit from design team	1 day	Tue 1/13/26	Tue 1/13/26											1/13	Architectu
92	Plumbing Final	1 day	Wed 1/7/26	Wed 1/7/26											1/7	Plumbing Fir
93	Electrical Final	1 day	Tue 1/6/26	Tue 1/6/26											1/6	Electrical Fin
94	HVAC Final	1 day	Tue 1/13/26	Tue 1/13/26											1/13	HVAC Fir
95	Fire Dept. Final	1 day	Wed 1/14/26	Wed 1/14/26											1/14	Fire Dept
96	Building Dept. Final	1 day	Thu 1/15/26	Thu 1/15/26											1/15	Building

ID	Task Model	Task Name	Duration	Current Start	Current Finish	<div><div></div><div>Jun</div><div>Jul</div><div>Qtr 3, 2025 Aug</div><div>Sep</div><div>Oct</div><div>Qtr 4, 2025 Nov</div><div>Dec</div><div>Jan</div></div>											
97		Apply for certificate of occupancy	4 days	Fri 1/16/26	Thu 1/22/26											1/16	App
98		Receive Certificate of Occupancy	1 day	Fri 1/23/26	Fri 1/23/26											1/23	Rec
99		Turnover	0 days	Fri 1/23/26	Fri 1/23/26											NA	Tu
