






Leader Bank
177 Main St Falmouth, MA

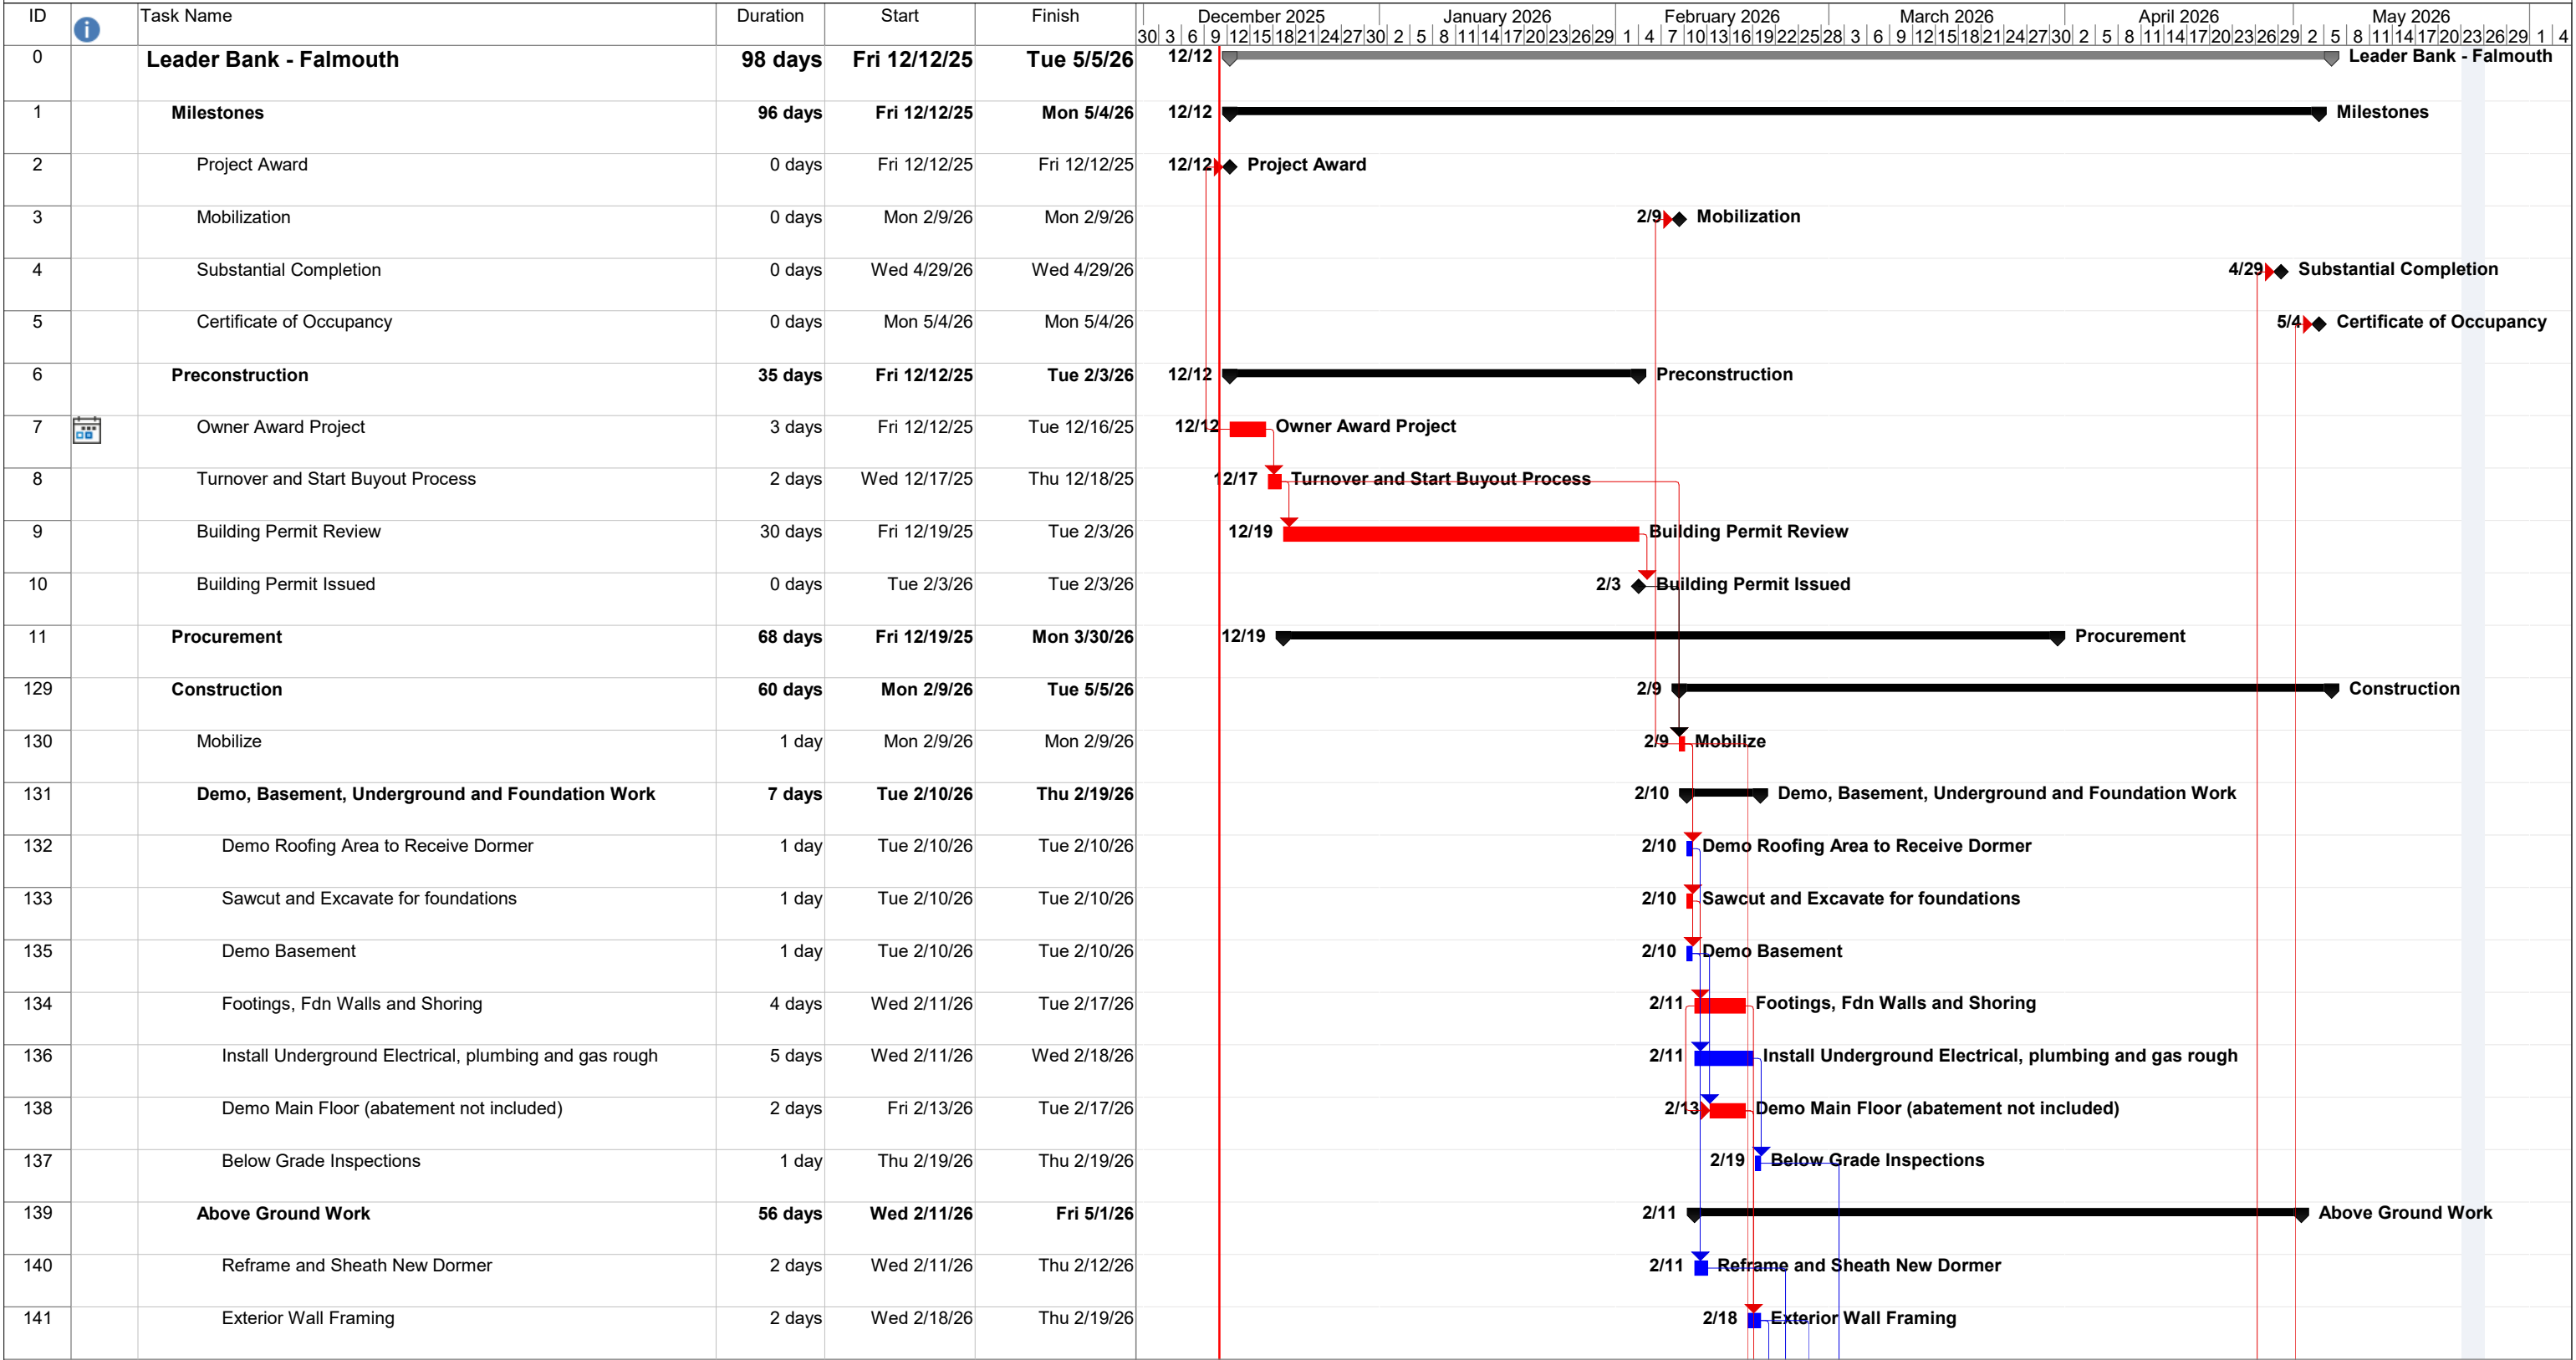

Leader Bank
177 Main St Falmouth, MA

ID		Task Name	Duration	Start	Finish	December 2025	January 2026	February 2026	March 2026	April 2026	May 2026
						30 3 6 9 12 15 18 21 24 27 30	2 5 8 11 14 17 20 23 26 29	1 4 7 10 13 16 19 22 25 28	3 6 9 12 15 18 21 24 27 30	2 5 8 11 14 17 20 23 26 29	2 5 8 11 14 17 20 23 26 29 1 4
144		Install Ductwork for HVAC Distribution	10 days	Wed 2/18/26	Tue 3/3/26			2/18	Install Ductwork for HVAC Distribution		
145		Layout and Approval	2 days	Wed 2/18/26	Thu 2/19/26			2/18	Layout and Approval		
142		Roof Sheathing at new bump outs	1 day	Fri 2/20/26	Fri 2/20/26			2/20	Roof Sheathing at new bump outs		
146		Frame Walls, Ceilings, Soffits	6 days	Fri 2/20/26	Fri 2/27/26			2/20	Frame Walls, Ceilings, Soffits		
143		Weather Tight Roof	2 days	Mon 2/23/26	Tue 2/24/26			2/23	Weather Tight Roof		
147		In-wall and hard ceiling electrical and Tele Data rough	7 days	Thu 2/26/26	Fri 3/6/26			2/26	In-wall and hard ceiling electrical and Tele Data rough		
148		Rough Plumbing Install Above Ground	5 days	Mon 3/2/26	Fri 3/6/26			3/2	Rough Plumbing Install Above Ground		
149		Install In-Wall Blocking	2 days	Thu 3/5/26	Fri 3/6/26			3/5	Install In-Wall Blocking		
150		Rough plumbing inspection	1 day	Mon 3/9/26	Mon 3/9/26			3/9	Rough plumbing inspection		
151		Rough Electrical inspection	1 day	Mon 3/9/26	Mon 3/9/26			3/9	Rough Electrical inspection		
152		Building dept rough framing inspection	1 day	Tue 3/10/26	Tue 3/10/26			3/10	Building dept rough framing inspection		
153		Insulation and Inspection	2 days	Wed 3/11/26	Thu 3/12/26			3/11	Insulation and Inspection		
154		Hang Drywall at All Walls	4 days	Fri 3/13/26	Wed 3/18/26			3/13	Hang Drywall at All Walls		
155		Install Drywall at Hard Ceilings	4 days	Fri 3/13/26	Wed 3/18/26			3/13	Install Drywall at Hard Ceilings		
156		Tape and Sand Drywall	7 days	Tue 3/17/26	Wed 3/25/26			3/17	Tape and Sand Drywall		
157		Prime and First Coat Paint Walls	4 days	Wed 3/25/26	Mon 3/30/26			3/25	Prime and First Coat Paint Walls		
163		Install ACT Grid	3 days	Fri 3/27/26	Tue 3/31/26			3/27	Install ACT Grid		
164		Install Light Fixtures	3 days	Mon 3/30/26	Wed 4/1/26			3/30	Install Light Fixtures		
165		Install HVAC Drops	2 days	Mon 3/30/26	Tue 3/31/26			3/30	Install HVAC Drops		
158		Install Electrical Outlets, and Tele Data Drops	3 days	Tue 3/31/26	Thu 4/2/26			3/31	Install Electrical Outlets, and Tele Data Drops		
159		Install Aluminum Door Frames and Glass	5 days	Tue 3/31/26	Mon 4/6/26			3/31	Install Aluminum Door Frames and Glass		
160		Install Ceramic Tiles, Grout at Bathrooms	3 days	Tue 3/31/26	Thu 4/2/26			3/31	Install Ceramic Tiles, Grout at Bathrooms		
162		Install electrical panels and branch circuits	3 days	Tue 3/31/26	Thu 4/2/26			3/31	Install electrical panels and branch circuits		
166		Above ceiling MEP Inspection @ ACT grid	1 day	Thu 4/2/26	Thu 4/2/26			4/2	Above ceiling MEP Inspection @ ACT grid		
161		Install Restroom & Janitor's closet plumbing Fixtures	3 days	Fri 4/3/26	Tue 4/7/26			4/3	Install Restroom & Janitor's closet plumbing Fixtures		

Leader Bank
177 Main St Falmouth, MA

ID		Task Name	Duration	Start	Finish	December 2025	January 2026	February 2026	March 2026	April 2026	May 2026
						30 3 6 9 12 15 18 21 24 27 30	2 5 8 11 14 17 20 23 26 29	1 4 7 10 13 16 19 22 25 28	3 6 9 12 15 18 21 24 27 30	2 5 8 11 14 17 20 23 26 29	1 4 7 10 13 16 19 22 25 28
167		Install ACT Tiles	2 days	Fri 4/3/26	Mon 4/6/26					4/3 ▶	▶
168		Install New VCT Flooring and Base	2 days	Fri 4/3/26	Mon 4/6/26					4/3 ▶	▶
169		Install New Carpets	5 days	Fri 4/3/26	Thu 4/9/26					4/3 ▶	▶
170		Install Millwork	4 days	Fri 4/10/26	Wed 4/15/26					4/10 ▶	▶
171		Install MEPs in Millwork	3 days	Thu 4/16/26	Tue 4/21/26					4/16 ▶	▶
172		Install Doors and Hardware	3 days	Thu 4/16/26	Tue 4/21/26					4/16 ▶	▶
173		Final Coat Paint Walls/Ceilings/Soffits	4 days	Wed 4/22/26	Mon 4/27/26					4/22 ▶	▶
174		Install Restroom Signage and Accessories	2 days	Fri 4/24/26	Mon 4/27/26					4/24 ▶	▶
175		Install Wall Finishes (Fire Extinguishers, Whiteboards, TVs etc	1 day	Fri 4/24/26	Fri 4/24/26					4/24 ▶	▶
176		Final Cleaning	1 day	Tue 4/28/26	Tue 4/28/26					4/28 ▶	▶
177		Assist bank with installing fixturing, technology and vault	3 days	Wed 4/29/26	Fri 5/1/26					4/29 ▶	▶
178		Inspections and Signoffs	8 days	Fri 4/24/26	Tue 5/5/26					4/24 ▶	▶
179		Architect & MEP Engineers Punchlist & Distribute	2 days	Fri 4/24/26	Mon 4/27/26					4/24 ▶	▶
180		Architect & MEP Engineers Affidavits	1 day	Tue 4/28/26	Tue 4/28/26					4/28 ▶	▶
185		Contractor Complete Punchlist	3 days	Tue 4/28/26	Thu 4/30/26					4/28 ▶	▶
181		Construction Substantial Completion	1 day	Wed 4/29/26	Wed 4/29/26					4/29 ▶	▶
183		Final Electrical/FA Inspection	1 day	Wed 4/29/26	Wed 4/29/26					4/29 ▶	▶
182		Final Plumbing Inspection	1 day	Thu 4/30/26	Thu 4/30/26					4/30 ▶	▶
184		Final Building Inspection	1 day	Fri 5/1/26	Fri 5/1/26					5/1 ▶	▶
186		Certificate of Occupancy	1 day	Mon 5/4/26	Mon 5/4/26					5/4 ▶	▶
187											
188		Turnover	1 day	Tue 5/5/26	Tue 5/5/26					5/5 ▶	▶
