


GARDEN CITY - EXPANSION VI - WS DEVELOPMENT

HILLSIDE RD CRANSTON RI

EXHIBIT NUMBER

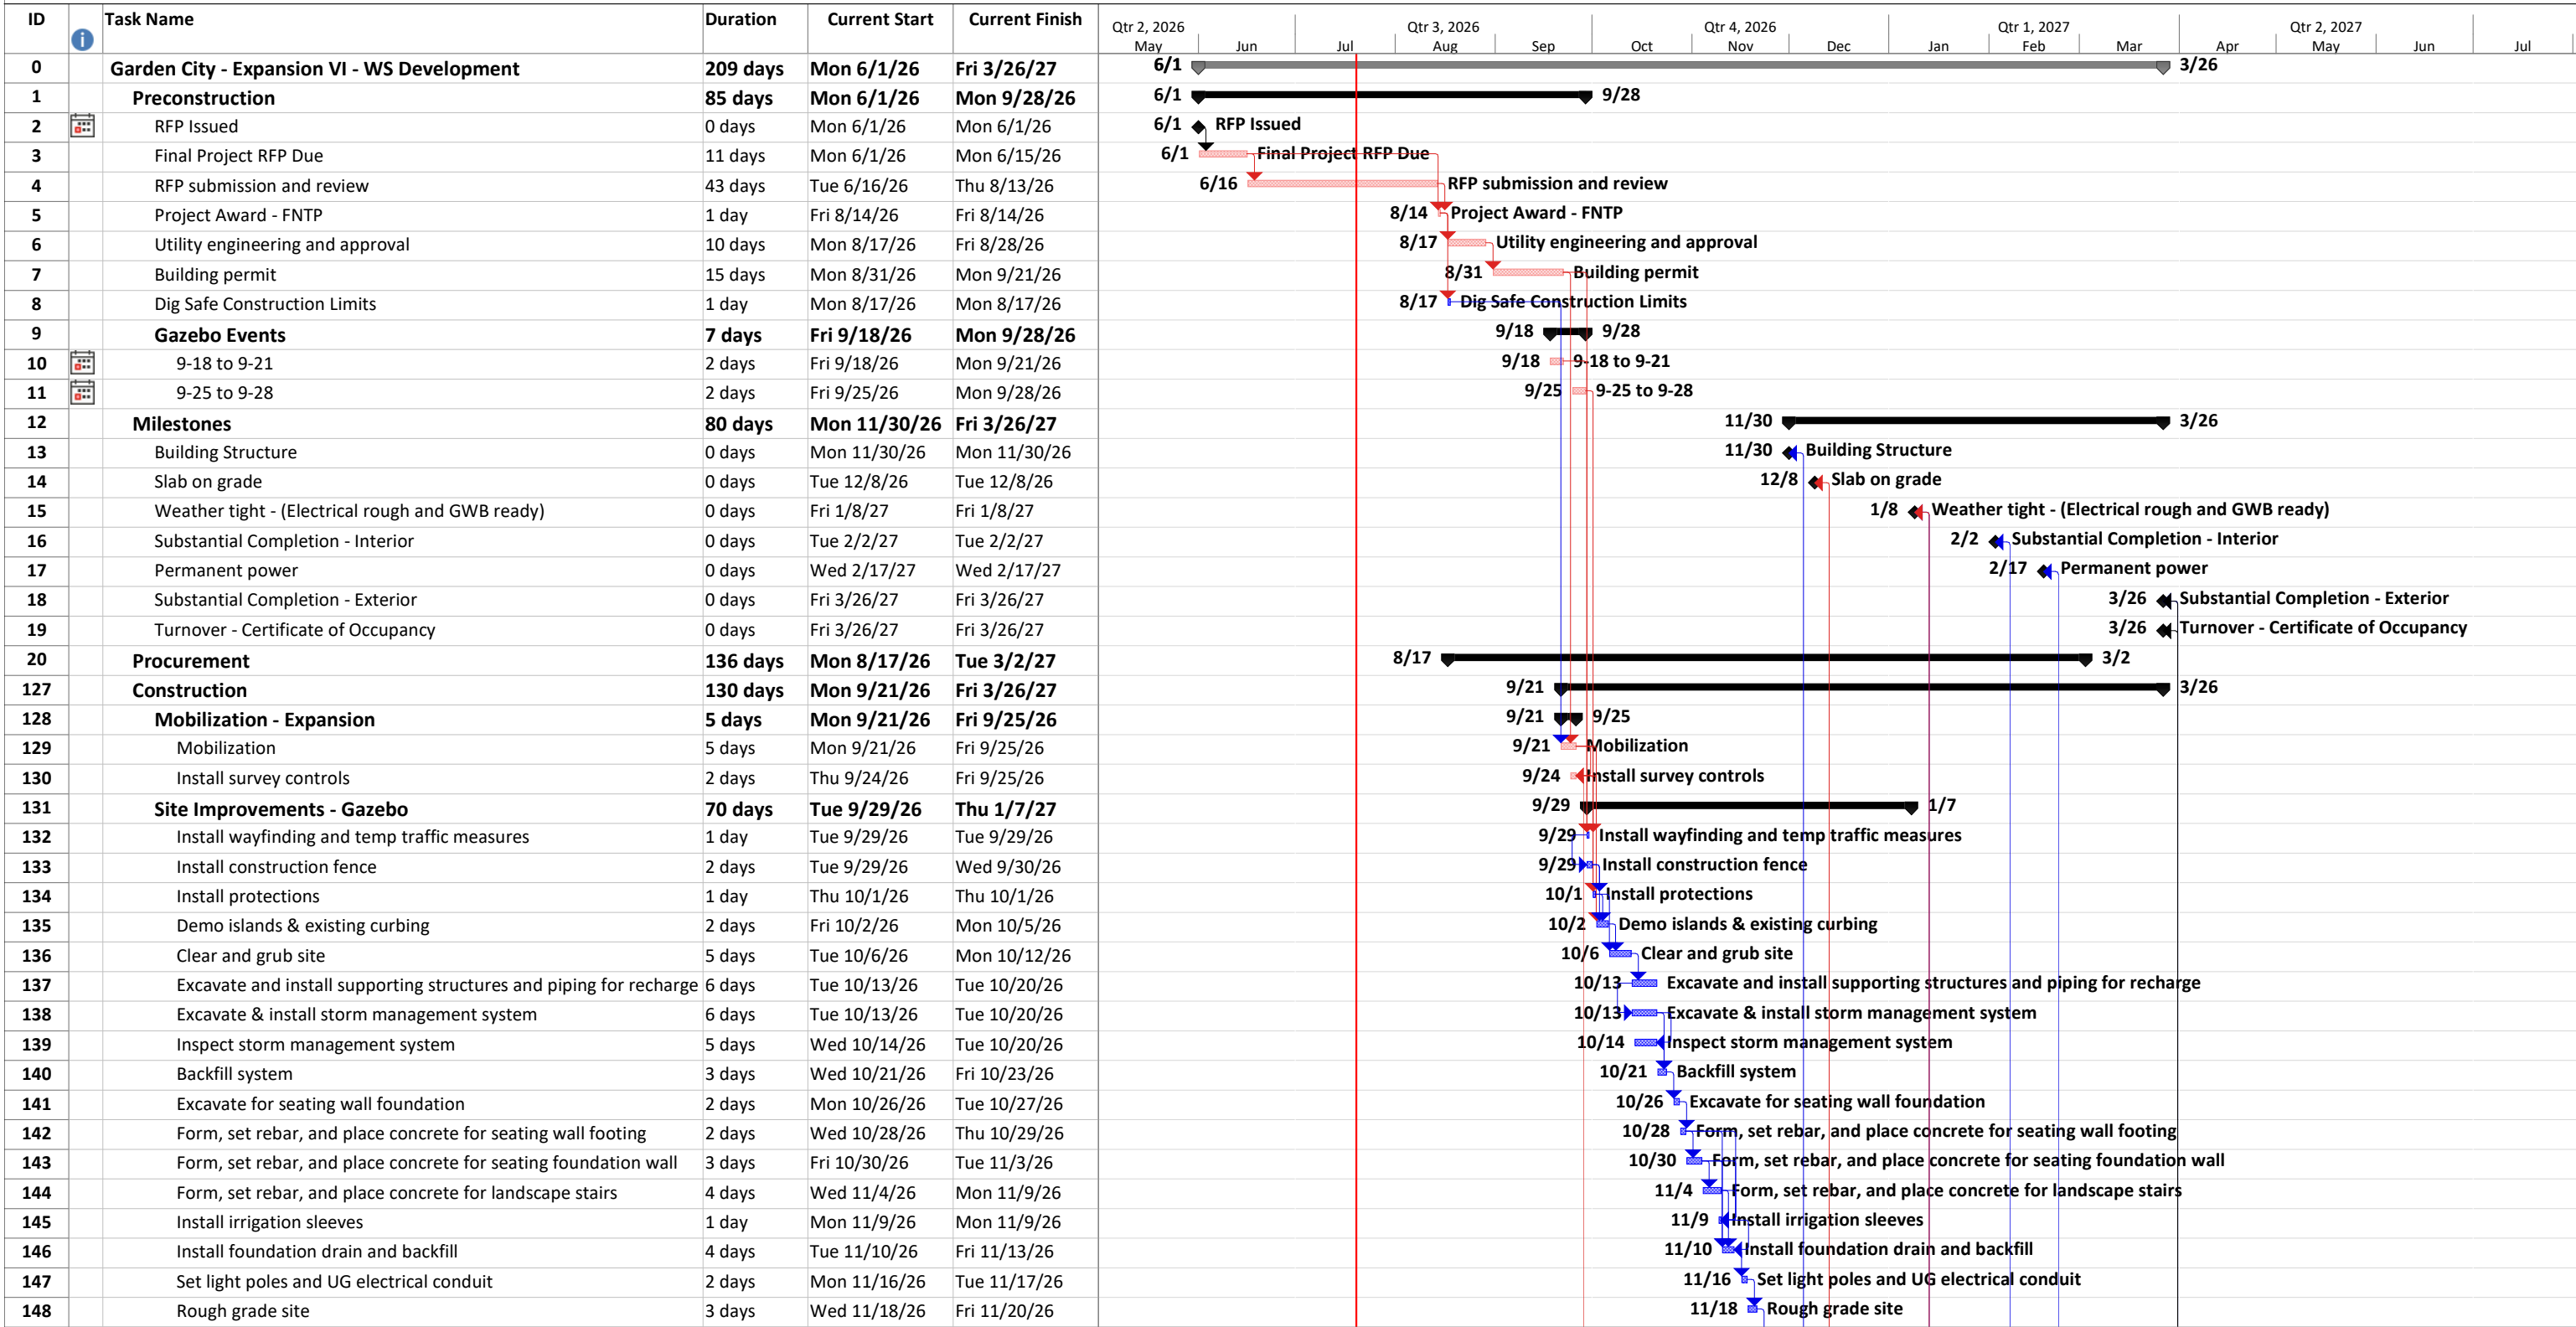

GARDEN CITY - EXPANSION VI - WS DEVELOPMENT
HILLSIDE RD CRANSTON RI

EXHIBIT NUMBER



GARDEN CITY - EXPANSION VI - WS DEVELOPMENT

HILLSIDE RD CRANSTON RI

EXHIBIT NUMBER

ID	Task Name	Duration	Current Start	Current Finish	Qtr 2, 2026			Qtr 3, 2026			Qtr 4, 2026		Qtr 1, 2027			Qtr 2, 2027		
					May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun
192	Backfill UG electrical conduit	1 day	Mon 11/30/26	Mon 11/30/26								11/30	Backfill UG electrical conduit					
193	Building Structure/Exterior Façade	70 days	Thu 11/12/26	Wed 2/24/27								11/12						2/24
194		Grout leveling plates	2 days	Thu 11/12/26	Fri 11/13/26							11/12	Grout leveling plates					
195		Erect structural steel	4 days	Mon 11/16/26	Thu 11/19/26							11/16	Erect structural steel					
196		Install Bar Joists	2 days	Fri 11/20/26	Mon 11/23/26							11/20	Install Bar Joists					
197	Steel decking install	3 days	Tue 11/24/26	Fri 11/27/26								11/24	Steel decking install					
198	Plumb and detail steel	1 day	Mon 11/30/26	Mon 11/30/26								11/30	Plumb and detail steel					
199	Install RTU blocking	2 days	Tue 12/1/26	Wed 12/2/26								12/1	Install RTU blocking					
200	Install RTU curbs	2 days	Tue 12/15/26	Wed 12/16/26								12/15	Install RTU curbs					
201	Install coverboard/vapor barrier	2 days	Thu 12/3/26	Fri 12/4/26								12/3	Install coverboard/vapor barrier					
202	Install roof insulation/TPO	6 days	Thu 12/3/26	Thu 12/10/26								12/3	Install roof insulation/TPO					
203	Install roof hatch	1 day	Thu 12/10/26	Thu 12/10/26								12/10	Install roof hatch					
204	Land RTU's	2 days	Thu 12/17/26	Fri 12/18/26								12/17	Land RTU's					
205	Install MEPs to RTU's	6 days	Mon 12/21/26	Tue 12/29/26								12/21	Install MEPs to RTU's					
206	Final grade for SOG	3 days	Tue 12/1/26	Thu 12/3/26								12/1	Final grade for SOG					
207	Install vapor barrier/mesh	2 days	Fri 12/4/26	Mon 12/7/26								12/4	Install vapor barrier/mesh					
208	Place SOG	1 day	Tue 12/8/26	Tue 12/8/26								12/8	Place SOG					
209	Install HM frames	2 days	Wed 12/9/26	Thu 12/10/26								12/9	Install HM frames					
210	Exterior LGMF install	10 days	Wed 12/9/26	Tue 12/22/26								12/9	Exterior LGMF install					
211	Install exterior sheathing	7 days	Mon 12/14/26	Tue 12/22/26								12/14	Install exterior sheathing					
212	Install storefront blocking	3 days	Wed 12/23/26	Mon 12/28/26								12/23	Install storefront blocking					
213	Install AVB	8 days	Tue 12/29/26	Fri 1/8/27								12/29	Install AVB					
214	Install rigid insulation	8 days	Thu 12/31/26	Tue 1/12/27								12/31	Install rigid insulation					
215	Install exterior blocking and furring	8 days	Tue 1/5/27	Thu 1/14/27								1/5	Install exterior blocking and furring					
216	Install storefront framing	3 days	Mon 1/11/27	Wed 1/13/27								1/11	Install storefront framing					
217	Install glazing	3 days	Thu 1/14/27	Tue 1/19/27								1/14	Install glazing					
218	Install storefront doors	2 days	Mon 1/11/27	Tue 1/12/27								1/11	Install storefront doors					
219	Install doors & hardware	2 days	Thu 1/14/27	Fri 1/15/27								1/14	Install doors & hardware					
220	Install granite base	8 days	Fri 1/15/27	Wed 1/27/27								1/15	Install granite base					
221	Install brick façade	15 days	Fri 1/15/27	Fri 2/5/27								1/15	Install brick façade					
222	Install canopy	3 days	Wed 2/3/27	Fri 2/5/27								2/3	Install canopy					
223	Install trim	5 days	Mon 2/8/27	Fri 2/12/27								2/8	Install trim					
224	Exterior painting	3 days	Tue 2/16/27	Thu 2/18/27								2/16	Exterior painting					
225	Install exterior lighting	2 days	Fri 2/19/27	Mon 2/22/27								2/19	Install exterior lighting					
226	Set scupper boxes & downspouts/install walkway pads	2 days	Thu 2/11/27	Fri 2/12/27								2/11	Set scupper boxes & downspouts/install walkway pads					
227	Install roof coping	2 days	Tue 2/16/27	Wed 2/17/27								2/16	Install roof coping					
228	Caulking throughout	2 days	Tue 2/23/27	Wed 2/24/27								2/23	Caulking throughout					
229	Interior	49 days	Mon 12/7/26	Wed 2/17/27								12/7						2/17
230	Frame interior partitions	8 days	Fri 12/11/26	Tue 12/22/26								12/11	Frame interior partitions					
231	Install sprinkler hangers/main lines	6 days	Mon 12/7/26	Mon 12/14/26								12/7	Install sprinkler hangers/main lines					
232	Install branch lines	6 days	Tue 12/15/26	Tue 12/22/26								12/15	Install branch lines					
233	Install sprinkler heads/FDC	5 days	Wed 12/23/26	Wed 12/30/26								12/23	Install sprinkler heads/FDC					
234	Plumbing rough	8 days	Mon 12/7/26	Wed 12/16/26								12/7	Plumbing rough					



GARDEN CITY - EXPANSION VI - WS DEVELOPMENT
HILLSIDE RD CRANSTON RI

EXHIBIT NUMBER

ID	Task Name	Duration	Current Start	Current Finish	Qtr 2, 2026 May	Jun	Jul	Qtr 3, 2026 Aug	Sep	Oct	Qtr 4, 2026 Nov	Dec	Jan	Qtr 1, 2027 Feb	Mar	Apr	Qtr 2, 2027 May	Jun	Jul
235	Install gas piping	8 days	Mon 12/21/26	Thu 12/31/26								12/21	12/21	1/4					
236	Plumbing rough inspection	1 day	Mon 1/4/27	Mon 1/4/27								12/21	1/4	1/4					
237	Electrical rough	8 days	Mon 12/21/26	Thu 12/31/26								12/21	12/21	1/4					
238	Fire Alarm rough	8 days	Mon 12/21/26	Thu 12/31/26								12/21	12/21	1/4					
239	Electrical/FA rough inspection	1 day	Mon 1/4/27	Mon 1/4/27								12/21	1/4	1/4					
240	Install insulation	6 days	Tue 1/5/27	Tue 1/12/27								12/21	1/5	1/5					
241	Install in wall blocking	2 days	Mon 1/11/27	Tue 1/12/27								12/21	1/11	1/11					
242	Rough framing/insulation building inspection	0 days	Tue 1/12/27	Tue 1/12/27								12/21	1/12	1/12					
243	Install GWB	6 days	Wed 1/13/27	Thu 1/21/27								12/21	1/13	1/13					
244	Tape/sand GWB	8 days	Fri 1/15/27	Wed 1/27/27								12/21	1/15	1/15					
245	Install interior lighting	5 days	Thu 1/28/27	Wed 2/3/27								12/21	1/28	1/28					
246	Install t-stats	3 days	Thu 1/28/27	Mon 2/1/27								12/21	1/28	1/28					
247	Install FA Control Panel	3 days	Thu 1/28/27	Mon 2/1/27								12/21	1/28	1/28					
248	Install FA devices	4 days	Thu 1/28/27	Tue 2/2/27								12/21	1/28	1/28					
249	Tie in FA System	2 days	Tue 2/2/27	Wed 2/3/27								12/21	2/2	2/2					
250	Install electrical panels	4 days	Thu 1/28/27	Tue 2/2/27								12/21	1/28	1/28					
251	Install transformers	3 days	Thu 1/28/27	Mon 2/1/27								12/21	1/28	1/28					
252	Install switchgear	5 days	Wed 2/3/27	Tue 2/9/27								12/21	2/3	2/3					
253	Permanent power	2 days	Tue 2/16/27	Wed 2/17/27								12/21	2/16	2/16					
254	Final Inspections, Close-out, Commissioning	62 days	Tue 12/1/26	Tue 3/2/27								12/1	12/1	3/2					
255	Commissioning	7 days	Thu 2/18/27	Fri 2/26/27								12/1	2/18	2/18					
256	NFPA 72 Record of Completion FA System	2 days	Thu 2/18/27	Fri 2/19/27								12/1	2/18	2/18					
257	Factory Startup Equipment	5 days	Thu 2/18/27	Wed 2/24/27								12/1	2/18	2/18					
258	Programming and Controls	2 days	Thu 2/25/27	Fri 2/26/27								12/1	2/25	2/25					
259	Close-out	6 days	Tue 2/23/27	Tue 3/2/27								12/1	2/23	2/23					
260	Punchlist walk for acceptance	5 days	Tue 2/23/27	Mon 3/1/27								12/1	2/23	2/23					
261	O&M Manuals	2 days	Thu 2/25/27	Fri 2/26/27								12/1	2/25	2/25					
262	Owner training	2 days	Mon 3/1/27	Tue 3/2/27								12/1	3/1	3/1					
263	Design Team Affidavits	62 days	Tue 12/1/26	Tue 3/2/27								12/1	12/1	3/2					
264	Structural Affidavit from design team	1 day	Tue 12/1/26	Tue 12/1/26								12/1	12/1	1/5					
265	Plumbing Affidavit from design team	1 day	Tue 1/5/27	Tue 1/5/27								12/1	1/5	1/5					
266	Mechanical Affidavit from design team	1 day	Mon 1/4/27	Mon 1/4/27								12/1	1/4	1/4					
267	Electrical/FA Affidavit from design team	1 day	Mon 2/22/27	Mon 2/22/27								12/1	2/22	2/22					
268	Architectural Affidavit from design team	1 day	Tue 3/2/27	Tue 3/2/27								12/1	3/2	3/2					
269	Final Inspections	56 days	Wed 1/6/27	Fri 3/26/27								12/1	1/6	1/6					
270	Plumbing Final	1 day	Wed 1/6/27	Wed 1/6/27								12/1	1/6	1/6					
271	Electrical Final	1 day	Tue 2/23/27	Tue 2/23/27								12/1	2/23	2/23					
272	HVAC Final	1 day	Mon 3/1/27	Mon 3/1/27								12/1	3/1	3/1					
273	Fire Dept. Final (Suppression/FA)	1 day	Tue 3/16/27	Tue 3/16/27								12/1	3/16	3/16					
274	Building Dept. Final	2 days	Wed 3/17/27	Thu 3/18/27								12/1	3/17	3/17					
275	Apply for Certificate of Occupancy	5 days	Fri 3/19/27	Thu 3/25/27								12/1	3/19	3/19					
276	Receive Certificate of Occupancy	1 day	Fri 3/26/27	Fri 3/26/27								12/1	3/26	3/26					
277																			



GARDEN CITY - EXPANSION VI - WS DEVELOPMENT

HILLSIDE RD CRANSTON RI

EXHIBIT NUMBER

ID	Task Name	Duration	Current Start	Current Finish	Qtr 2, 2026 May	Jun	Jul	Qtr 3, 2026 Aug	Sep	Oct	Qtr 4, 2026 Nov	Dec	Jan	Qtr 1, 2027 Feb	Mar	Apr	Qtr 2, 2027 May	Jun	Jul
278	Turnover - TCO	0 days	Fri 3/26/27	Fri 3/26/27											NA				
