


BRIXMOR - BURLINGTON, MA SCHEDULE

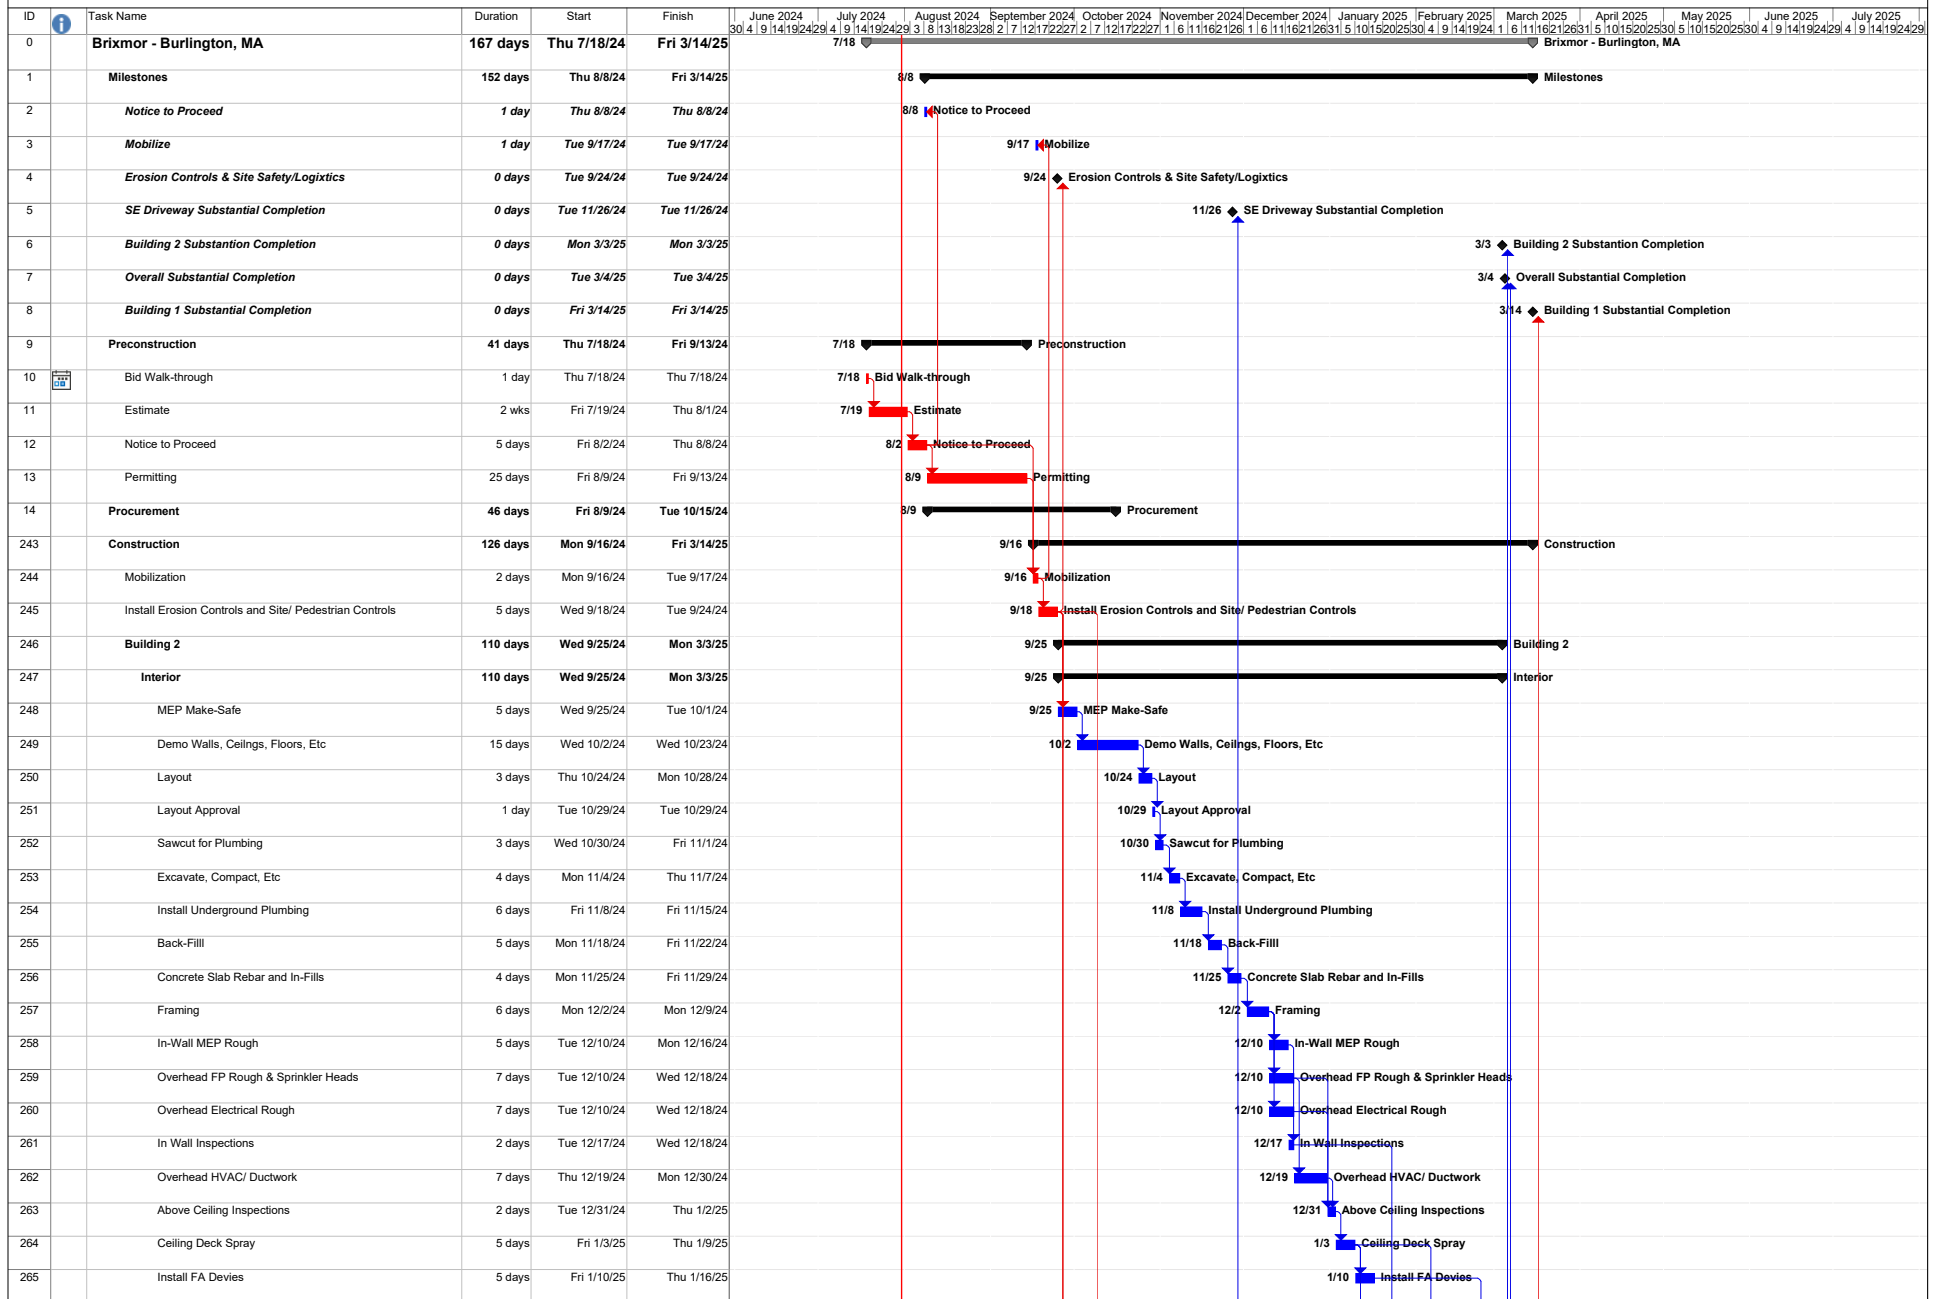

BRIXMOR - BURLINGTON, MA SCHEDULE

ID	Task Name	Duration	Start	Finish	June 2024	July 2024	August 2024	September 2024	October 2024	November 2024	December 2024	January 2025	February 2025	March 2025	April 2025	May 2025	June 2025	July 2025
266	Install Lighting	7 days	Fri 1/10/25	Mon 1/20/25								1/10	1/15	1/20				
267	Install RGDs	3 days	Fri 1/10/25	Tue 1/14/25								1/10	1/14	1/17				
268	Board & Tape	5 days	Thu 1/23/25	Wed 1/29/25								1/23	1/28	2/2				
269	Prime and First Coat Paint	5 days	Thu 1/30/25	Wed 2/5/25								1/30	2/4	2/9				
270	Final Walls Paint Coat	5 days	Thu 2/6/25	Wed 2/12/25								2/6	2/11	2/16				
271	Final Cleaning	6 days	Thu 2/13/25	Thu 2/20/25								2/13	2/18	2/23				
272	Final MEP Deicing	7 days	Thu 2/13/25	Fri 2/21/25								2/13	2/18	2/23				
273	Final Inspections	5 days	Mon 2/24/25	Fri 2/28/25								2/24	2/28	3/3				
274	Building 2 - Interior Substantial Completion	1 day	Mon 3/3/25	Mon 3/3/25								3/3						
275	Sitework & Exterior	111 days	Wed 9/25/24	Tue 3/4/25	9/25													
276	SE Driveway	44 days	Wed 9/25/24	Tue 11/26/24	9/25													
277	Install Traffic Controls	3 days	Wed 9/25/24	Fri 9/27/24	9/25													
278	Salage Existing Signage to be reused	3 days	Wed 9/25/24	Fri 9/27/24	9/25													
279	Demo and Remove Curbing/ Islands	3 days	Mon 9/30/24	Wed 10/2/24	9/30													
280	Surveyor Markings	2 days	Thu 10/3/24	Fri 10/4/24	10/3													
281	Mill existing pavement/ Prep for Site improvements/ Grade Changes	3 days	Thu 10/3/24	Mon 10/7/24	10/3													
282	Regrade Site	5 days	Tue 10/8/24	Tue 10/15/24	10/8													
283	Install Flush Granite Curbs for Stamped walkway	3 days	Wed 10/16/24	Fri 10/18/24	10/16													
284	Paving Binder	3 days	Mon 10/21/24	Wed 10/23/24	10/21													
285	Install Concrete Curbs and Walks	6 days	Thu 10/24/24	Thu 10/31/24	10/24													
286	Site Lighting	3 days	Fri 11/1/24	Tue 11/5/24	11/1													
287	Red Stamped Asphalt with flush granite curbs	2 days	Fri 11/1/24	Mon 11/4/24	11/1													
288	Irrigation	5 days	Wed 11/6/24	Tue 11/12/24	11/6													
289	Loam and Landscape Plantings	3 days	Wed 11/13/24	Fri 11/15/24	11/13													
290	Pave Top Course	4 days	Mon 11/18/24	Thu 11/21/24	11/18													
291	Install Signage	2 days	Fri 11/22/24	Mon 11/25/24	11/22													
292	Install Striping	2 days	Fri 11/22/24	Mon 11/25/24	11/22													
293	SE Driveway Substantial Completion	1 day	Tue 11/26/24	Tue 11/26/24	11/26													
294	Exterior/ Façade	110 days	Thu 9/26/24	Tue 3/4/25	9/26													
295	Make Safe	4 days	Thu 9/26/24	Tue 10/1/24	9/26													
296	Scaffolding/ Overhead Protection	5 days	Wed 10/2/24	Tue 10/8/24	10/2													
297	Install Shoring	4 days	Wed 10/2/24	Mon 10/7/24	10/2													
298	Demo Storefront & Façade	10 days	Wed 10/9/24	Wed 10/23/24	10/9													
299	Temp Weather Protection	3 days	Thu 10/24/24	Mon 10/28/24	10/24													
300	Layout	4 days	Tue 10/29/24	Fri 11/1/24	10/29													
301	New Metal Framing, Insulate and Sheath including Parapets	20 days	Mon 11/4/24	Mon 12/2/24	11/4													
302	Install Drains, Cleanouts, etc	7 days	Tue 12/3/24	Wed 12/11/24	12/3													

BRIXMOR - BURLINGTON, MA SCHEDULE

ID	Task Name	Duration	Start	Finish	June 2024	July 2024	August 2024	September 2024	October 2024	November 2024	December 2024	January 2025	February 2025	March 2025	April 2025	May 2025	June 2025	July 2025
303	Install Roofing	15 days	Tue 12/3/24	Mon 12/23/24							12/3	12/4	12/5	12/6	12/7	12/8	12/9	12/10
304	Install New AVB & Water-Proofing	7 days	Thu 12/12/24	Fri 12/20/24							12/12	12/13	12/14	12/15	12/16	12/17	12/18	12/19
305	New Exterior Façade/ Siding	10 days	Tue 12/24/24	Wed 1/8/25							12/24	12/25	12/26	12/27	12/28	12/29	12/30	1/1
306	Exterior Paint	10 days	Thu 1/9/25	Wed 1/22/25							1/9	1/10	1/11	1/12	1/13	1/14	1/15	1/16
307	Install Masonry	6 days	Thu 1/9/25	Thu 1/16/25							1/9	1/10	1/11	1/12	1/13	1/14	1/15	1/16
308	Install New Storefronts	10 days	Thu 1/9/25	Wed 1/22/25							1/9	1/10	1/11	1/12	1/13	1/14	1/15	1/16
309	Weather Tight	1 day	Thu 1/9/25	Thu 1/9/25							1/9	1/10	1/11	1/12	1/13	1/14	1/15	1/16
310	Remove Shoring	2 days	Thu 1/23/25	Fri 1/24/25							1/23	1/24	1/25	1/26	1/27	1/28	1/29	1/30
311	New Sidewalks & Sidewalk Patching	10 days	Mon 1/27/25	Fri 2/7/25							1/27	1/28	1/29	1/30	2/1	2/2	2/3	2/4
312	Caulking and Sealants at Exterior Systems	6 days	Mon 2/10/25	Mon 2/17/25							2/10	2/11	2/12	2/13	2/14	2/15	2/16	2/17
313	Install New Light Fixtures	5 days	Tue 2/18/25	Mon 2/24/25							2/18	2/19	2/20	2/21	2/22	2/23	2/24	2/25
314	Remove Pedestrian Overhead Protection and	2 days	Tue 2/25/25	Wed 2/26/25							2/25	2/26	2/27	2/28	2/29	2/30	3/1	3/2
315	Final Inspections	3 days	Thu 2/27/25	Mon 3/3/25							2/27	2/28	2/29	2/30	3/1	3/2	3/3	3/4
316	Substantial Completion	1 day	Tue 3/4/25	Tue 3/4/25							3/4	3/5	3/6	3/7	3/8	3/9	3/10	3/11
317	SW Patios & Screen Wall	63 days	Mon 9/30/24	Mon 12/30/24					9/30	10/1	10/2	10/3	10/4	10/5	10/6	10/7	10/8	10/9
318	Survey Markings/Layout	2 days	Mon 9/30/24	Tue 10/1/24					9/30	10/1	10/2	10/3	10/4	10/5	10/6	10/7	10/8	10/9
319	Excavate for Foundations and Prep for Walkways	6 days	Wed 10/2/24	Wed 10/9/24					10/2	10/3	10/4	10/5	10/6	10/7	10/8	10/9	10/10	10/11
320	Compact and Prep	6 days	Thu 10/10/24	Fri 10/18/24					10/10	10/11	10/12	10/13	10/14	10/15	10/16	10/17	10/18	10/19
321	Form & Rebar	5 days	Mon 10/21/24	Fri 10/25/24					10/21	10/22	10/23	10/24	10/25	10/26	10/27	10/28	10/29	10/30
322	Pour Concrete Foundations/ Footings	10 days	Mon 10/28/24	Fri 11/8/24					10/28	10/29	10/30	10/31	11/1	11/2	11/3	11/4	11/5	11/6
323	Install New Concrete Walkway	10 days	Mon 10/28/24	Fri 11/8/24					10/28	10/29	10/30	10/31	11/1	11/2	11/3	11/4	11/5	11/6
324	Install New Patios	10 days	Mon 11/11/24	Fri 11/22/24					11/11	11/12	11/13	11/14	11/15	11/16	11/17	11/18	11/19	11/20
325	Backfill and Grade	5 days	Mon 11/11/24	Fri 11/15/24					11/11	11/12	11/13	11/14	11/15	11/16	11/17	11/18	11/19	11/20
326	Install Screen Structural Steel and Tie-Ins	10 days	Mon 11/18/24	Mon 12/2/24					11/18	11/19	11/20	11/21	11/22	11/23	11/24	11/25	11/26	11/27
327	Install Screen Wall	8 days	Tue 12/3/24	Thu 12/12/24					12/3	12/4	12/5	12/6	12/7	12/8	12/9	12/10	12/11	12/12
328	Loam and Plant and Seed	10 days	Fri 12/13/24	Fri 12/27/24					12/13	12/14	12/15	12/16	12/17	12/18	12/19	12/20	12/21	12/22
329	Substantial Completion	1 day	Mon 12/30/24	Mon 12/30/24					12/30	12/31	1/1	1/2	1/3	1/4	1/5	1/6	1/7	1/8
330	NE Islands	31 days	Tue 10/8/24	Wed 11/20/24					10/8	10/9	10/10	10/11	10/12	10/13	10/14	10/15	10/16	10/17
331	Sawcut Excavate and Prep	5 days	Tue 10/8/24	Tue 10/15/24					10/8	10/9	10/10	10/11	10/12	10/13	10/14	10/15	10/16	10/17
332	Grade and Compact	5 days	Wed 10/16/24	Tue 10/22/24					10/16	10/17	10/18	10/19	10/20	10/21	10/22	10/23	10/24	10/25
333	Install Flush Curbing	4 days	Wed 10/23/24	Mon 10/28/24					10/23	10/24	10/25	10/26	10/27	10/28	10/29	10/30	10/31	11/1
334	Intall Concrete Sidewalk	6 days	Tue 10/29/24	Tue 11/5/24					10/29	10/30	10/31	11/1	11/2	11/3	11/4	11/5	11/6	11/7
335	Install Stamped Paving/ Pavers	6 days	Wed 11/6/24	Wed 11/13/24					11/6	11/7	11/8	11/9	11/10	11/11	11/12	11/13	11/14	11/15
336	Paving/ Patch Paving	5 days	Thu 11/14/24	Wed 11/20/24					11/14	11/15	11/16	11/17	11/18	11/19	11/20	11/21	11/22	11/23
337	Building 1	109 days	Wed 10/9/24	Fri 3/14/25					10/9	10/10	10/11	10/12	10/13	10/14	10/15	10/16	10/17	10/18
338	Exterior/ Façade	109 days	Wed 10/9/24	Fri 3/14/25					10/9	10/10	10/11	10/12	10/13	10/14	10/15	10/16	10/17	10/18
339	Make Safe	4 days	Wed 10/9/24	Tue 10/15/24					10/9	10/10	10/11	10/12	10/13	10/14	10/15	10/16	10/17	10/18
340	Scaffolding/ Overhead Protection	4 days	Wed 10/16/24	Mon 10/21/24					10/16	10/17	10/18	10/19	10/20	10/21	10/22	10/23	10/24	10/25

BRIXMOR - BURLINGTON, MA SCHEDULE

ID	Task Name	Duration	Start	Finish	June 2024	July 2024	August 2024	September 2024	October 2024	November 2024	December 2024	January 2025	February 2025	March 2025	April 2025	May 2025	June 2025	July 2025
341	Install Shoring	4 days	Wed 10/16/24	Mon 10/21/24	30	4	9	14	19	24	29	4	9	14	19	24	29	3
342	Demo Roof & Façade Structures	10 days	Tue 10/22/24	Mon 11/4/24					10	16	22	28	3	9	15	21	27	3
343	Temp Weather Protection	3 days	Tue 11/5/24	Thu 11/7/24					11	5	8							
344	Layout	4 days	Fri 11/8/24	Wed 11/13/24					11	8	11	14	18	21	25	28	31	3
345	New Mtl Framing, Insulat and Sheath Including Parapets	20 days	Thu 11/14/24	Thu 12/12/24					11	14	18	21	25	28	31	3	6	10
346	Install Drains, Cleanouts, etc	7 days	Fri 12/13/24	Mon 12/23/24					12	13	16	20	23	27	30	31		
347	Install Roofing	15 days	Fri 12/13/24	Mon 1/6/25					12	13	16	20	23	27	30	31		
348	Install New AVB & Water-Proofing	7 days	Tue 12/24/24	Fri 1/3/25					12	24	27	30	31					
349	New Exterior Façade/ Siding	10 days	Tue 1/7/25	Mon 1/20/25					1	7	10	14	17	21	24	28	31	3
350	Exterior Paint	10 days	Tue 1/21/25	Mon 2/3/25					1	21	24	28	31					
351	Install Masonry	6 days	Tue 1/21/25	Tue 1/28/25					1	21	24	28	31					
352	Install New Storefronts	5 days	Tue 1/21/25	Mon 1/27/25					1	21	24	28	31					
353	Weather Tight	1 day	Tue 1/21/25	Tue 1/21/25					1	21	21	21	21					
354	Remove Shoring	2 days	Tue 2/4/25	Wed 2/5/25					2	4	5	5	5					
355	New Sidewalks & Sidewalk Patching	10 days	Thu 2/6/25	Wed 2/19/25					2	6	10	13	17	20	24	27	31	3
356	Caulking and Sealants at Exterior Systems	6 days	Thu 2/20/25	Thu 2/27/25					2	20	23	26	27	30	31			
357	Install New Light Fixtures	5 days	Fri 2/28/25	Thu 3/6/25					2	28	30	31	3	6	9	12	15	18
358	Remove Pedestrian Overhead Protection and	2 days	Fri 3/7/25	Mon 3/10/25					3	7	8	8	8					
359	Final Inspections	3 days	Tue 3/11/25	Thu 3/13/25					3	11	12	13	14	15	16	17	18	21
360	Substantial Completion	1 day	Fri 3/14/25	Fri 3/14/25					3	14	14	14	14	14	14	14	14	14
